ID	Task Name	Duration	Start	Finish
1	LOA 14 Start Date	0 days	Mon 2/2/15	Mon 2/2/15
2	**Release 6.2**	**86 days**	**Mon 2/2/15**	**Mon 6/1/15**
3	Requirements	5 days	Mon 2/2/15	Fri 2/6/15
4	**Enhancements**	**86 days**	**Mon 2/2/15**	**Mon 6/1/15**
5	Response Plan Templates	22 days	Mon 2/2/15	Tue 3/3/15
6	DMS Force Caps	4 days	Wed 3/4/15	Mon 3/9/15
7	DMS Force Blank	12 days	Sat 5/16/15	Mon 6/1/15
8	Dismiss Redundant TSS Alerts	23 days	Sat 3/21/15	Tue 4/21/15
9	**Arterial Probe Algorithm**	**52 days**	**Sat 3/7/15**	**Tue 5/19/15**
10	Release 6.0	35 days	Sat 3/7/15	Thu 4/23/15
11	Release 6.1	5 days	Tue 4/28/15	Mon 5/4/15
12	Release 6.2	5 days	Tue 5/12/15	Mon 5/18/15
13	Optional TSS Link Configuration ir	18 days	Sat 4/25/15	Tue 5/19/15
14	**Project Management**	**52 days**	**Mon 2/2/15**	**Tue 4/14/15**
15	SRS	8 days	Mon 2/2/15	Wed 2/11/15
16	SDD	10 days	Thu 2/12/15	Wed 2/25/15
17	SIP	7 days	Mon 3/9/15	Tue 3/17/15
18	SICP	20 days	Wed 3/18/15	Tue 4/14/15
19	VDD	10 days	Mon 3/9/15	Fri 3/20/15
20	SUM	8 days	Mon 3/30/15	Wed 4/8/15
21	LOA 14 Supplement 1 Start Date	0 days	Mon 7/6/15	Mon 7/6/15
22	**Release 6.2 - Phase 2**	**75 days**	**Mon 7/6/15**	**Fri 10/16/15**
23	**Small Enhancements**	**47 days**	**Mon 7/6/15**	**Tue 9/8/15**
36	WAZE Phase 2	40 days	Mon 8/24/15	Fri 10/16/15
37	WWD Phase 2	40 days	Mon 7/6/15	Fri 8/28/15
38	Discontinuous Lane Blockage	10 days	Fri 7/31/15	Thu 8/13/15
39	**Release Documentation and Testing**	**141 days**	**Fri 8/14/15**	**Fri 2/26/16**
40	**Project Management**	**27 days**	**Mon 10/5/15**	**Tue 11/10/15**
41	SRS	8 days	Fri 8/14/15	Tue 8/25/15
42	SDD	10 days	Thu 10/15/15	Wed 10/28/15
43	SIP	7 days	Mon 10/5/15	Tue 10/13/15
44	**SICP**	**20 days**	**Wed 10/14/15**	**Tue 11/10/15**
45	SICP Draft Due	0 days	Wed 10/14/15	Wed 10/14/15
46	VDD/IN	10 days	Mon 10/5/15	Fri 10/16/15
47	SUM	8 days	Mon 10/5/15	Wed 10/14/15
48	ICDs	3 days	Mon 10/5/15	Wed 10/7/15
49	ERWIN Model Delivery	0 days	Wed 10/14/15	Wed 10/14/15
50	**Release Planning**	**98 days**	**Wed 10/14/15**	**Fri 2/26/16**
51	PCA	**2 days**	**Wed 10/28/15**	**Thu 10/29/15**
52	Setup and Walk-through	2 days	Wed 10/28/15	Thu 10/29/15

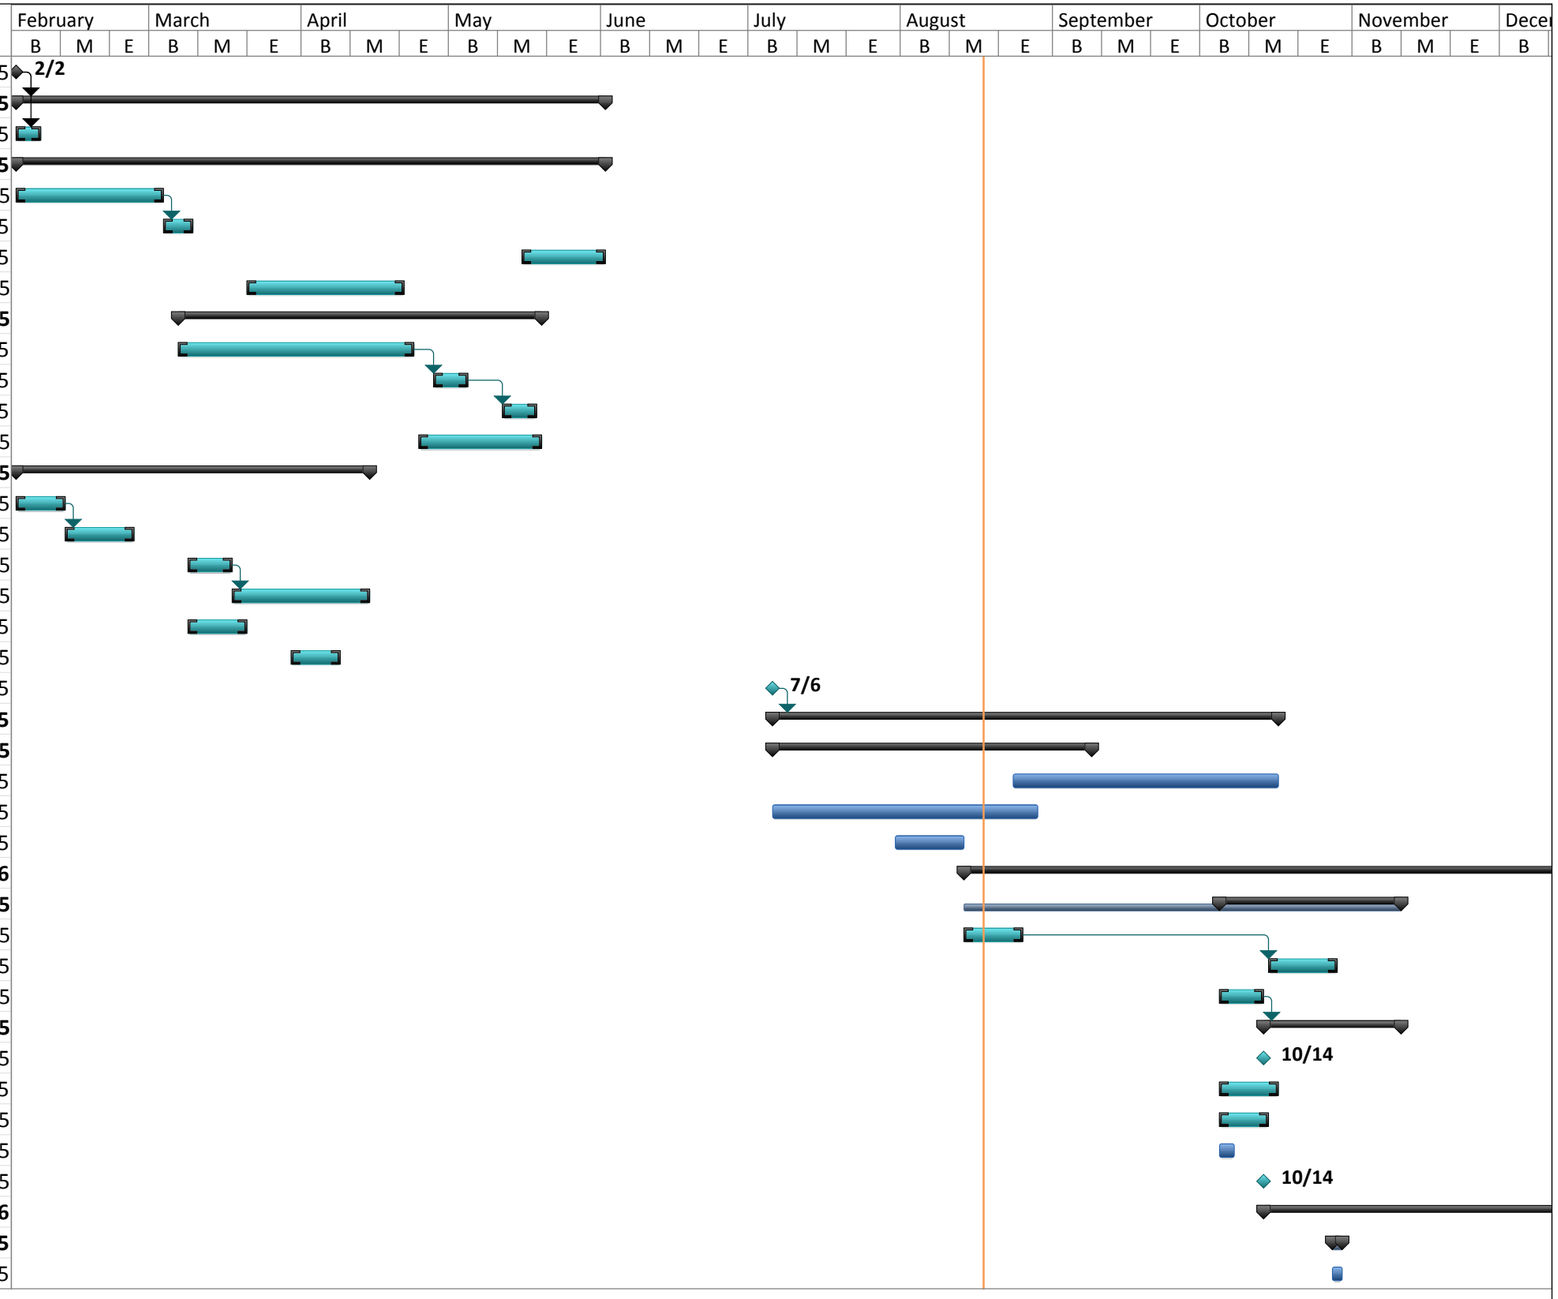

Project: Release 6.2 Schedule new
Date: Tue 8/18/15

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline	
Split	External Tasks	Inactive Summary	Manual Summary	Progress	
Milestone	External Milestone	Manual Task	Start-only		
Summary	Inactive Task	Duration-only	Finish-only		

ID		Task Name	Duration	Start	Finish
53		Acceptance Testing	**39 days**	**Wed 10/14/15**	**Mon 12/7/15**
54		FAT	**23 days**	**Wed 10/14/15**	**Fri 11/13/15**
55		FAT Setup	18 days	Wed 10/14/15	Fri 11/6/15
56		Conduct FAT	5 days	Mon 11/9/15	Fri 11/13/15
57		SICP CAP	**16 days**	**Mon 11/16/15**	**Mon 12/7/15**
58		Produce Defect List & Remedy	1 day	Mon 11/16/15	Mon 11/16/15
59		Corrective Actions	12 days	Tue 11/17/15	Wed 12/2/15
60		Produce Installer, Update VDD	3 days	Thu 12/3/15	Mon 12/7/15
61		IV&V	55 days	Mon 12/14/15	Fri 2/26/16

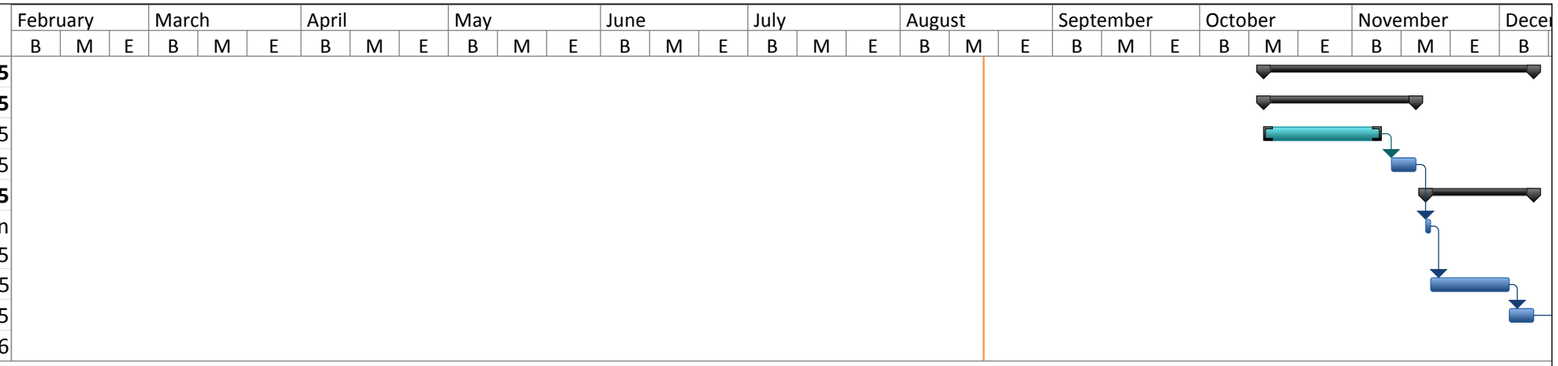

Project: Release 6.2 Schedule new
Date: Tue 8/18/15

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline			
Split	External Tasks	Inactive Summary	Manual Summary	Progress			
Milestone	External Milestone	Manual Task	Start-only				
Summary	Inactive Task	Duration-only	Finish-only				
